

Arboricultural Method Statement

*relating to development at
West Sompting Phase 3
West Sussex*

Client
Persimmon

May 2026

2555-KC-XX-YTREE-MethodStatement-Rev0

The Studio, Timbers, Gables Road, Church Crookham, Fleet, Hampshire, GU52 6QY
Telephone +44(0)1252 850096 | Email: admin@keenconsultants.co.uk

Keen Consultants is a trading name of Keen (Europe) Limited. Registered No. 12641584
Registered office: The Stables, Moneys Farm, Bottle Lane, Mattingley, Hampshire, RG27 8LI



© **Keen Consultants**

The copyright of this document resides with Keen Consultants unless assigned in writing by the company.

Document history

Revision	Issue Status	Details	Approved/Date
Rev0	Final	Initial report	JK / 12 May 2026

Contents

1.0	Statement of purpose.....	5
2.0	Related documents and drawings	5
3.0	Arboricultural issues & implications	6
4.0	Facilitation tree works	6
5.0	General site care	6
6.0	Sequencing of works	7
7.0	Protective barriers and ground protection	8
8.0	Treatment of existing hard surfaces	8
9.0	Creation of new hard surfacing within root protection areas	8
10.0	Excavations within root protection areas.....	10
11.0	Reinstatement and landscaping	10
12.0	Planning, communication and supervision	10
13.0	Transgression.....	11
14.0	Conclusion.....	12

Appendices

Appendix 1

Typical detail of no-dig construction

Appendix 2

List of contacts

Tables

Table 1: Documents referred to	5
Table 2: Drawings referred to	5

ABSTRACT

Protective barriers are required throughout the construction process to protect the retained trees on the site.

Tree removal and pruning are required.

Sections of hard surface are located within root protection areas and require specialist construction.

Utility installation is required within root protection areas and specialist installation techniques are required.

1.0 Statement of purpose

- 1.1 The purpose of this method statement is to demonstrate how works will be undertaken at Phase 3, West Sompting, West Sussex to avoid unacceptable arboricultural impact and provide an adequate level of protection for those trees that are to be retained.
- 1.2 This method statement has been produced for Persimmon in order to inform the construction team and satisfy the requirements of the Local Planning Authority (LPA) Adur District Council. The works are the subject of a planning application and this arboricultural method statement has been prepared to support the application.
- 1.3 This method statement merely considers the systems of work in relation to the health and safety of retained trees. It does not address requirements of the Health and Safety Executive that should be considered in detail by those parties involved.

2.0 Related documents and drawings

- 2.1 This method statement should be read in conjunction with the documents in Table 1 below.

Table 1: Documents referred to

Originator	Title/Reference
British Standards Institute	BS5837:2012 Trees in relation to design, demolition and construction – Recommendations

and the following drawings in Table 2

Table 2: Drawings referred to

Originator	Drg No	Title
Persimmon	612_PL_100_Ph3	Site Layout
Keen Consultants	2555-KC-XX-YTREE-TCP01Rev0	Tree Constraints Plan
Keen Consultants	2555-KC-XX-YTREE-TPP01Rev0	Tree Protection Plan

3.0 Arboricultural issues & implications

- 3.1 Detail of the trees and their protection are discussed and detailed in the documents, and shown on the drawings, listed above and should be read in conjunction with this method statement.
- 3.2 The buildings are located outside the root protection areas of all retained trees and can therefore be constructed using conventional construction techniques.
- 3.3 Sections of proposed hard surface extend within the root protection area of retained trees requiring the adoption of specific construction techniques.
- 3.4 Tree removal and pruning work is required.
- 3.5 Utility provision is required within root protection areas and therefore needs to be installed using specialist measures to avoid harm to the retained trees.
- 3.6 Monitoring of works is required.

4.0 Facilitation tree works

- 4.1 Tree pruning and removal are required to accommodate the proposed development.
- 4.2 Details of the tree work are given in the schedule on the Tree Protection Plan referred to in Table 2 above.
- 4.3 All tree work shall be undertaken in accordance with *BS3998:2010:Tree Work – Recommendations*.

5.0 General site care

- 5.1 To ensure that the trees to be retained are afforded an adequate degree of protection during the works, the following general precautions will be observed:
 - 5.1.1 No fires will be lit on site

- 5.1.2 No access will be permitted within the temporarily barriered areas, unless and only where otherwise approved herein. Ground levels will not be changed within them and existing vegetation and topsoil will be left undisturbed but may be treated with approved herbicides if eradication is required.
- 5.1.3 No materials, equipment or debris will be stored within any of the barriered areas and no chemicals, petrol or diesel will be allowed to spill where they may contaminate the root protection areas of retained trees.
- 5.1.4 All heavy plant, machinery, cranes and delivery vehicles shall be excluded from the areas demarcated for protection on the Tree Protection Plan.

6.0 Sequencing of works

- 6.1 A logical sequence of events is to be observed as follows:

- Stage 1 Pre-commencement site meeting (See Section 12).
- Stage 2 Undertake tree works.
- Stage 3 Erect protective barriers as shown on the drawing in Table 2 (specifications given in Section 7).
- Stage 4 Install power cables
- Stage 5 Implement areas of no-dig construction (in accordance with site progress).
- Stage 6 Implement development construction.
- Stage 7 Take down protective barriers and complete soft landscape works.

7.0 Protective barriers and ground protection

- 7.1 Temporary barriers will be erected as indicated on the Tree Protection Plan listed in Table 2. The specification for this barriers will be in accordance with the recommendations given in *BS5837:2012 Trees in relation to design, demolition and construction – Recommendations* Section 6.2 and will comprise 2.0m mesh barriers (Heras type panels are a simple, readily available solution) attached to a scaffold framework. Support scaffolds will be attached to the scaffold framework as necessary at an angle of 45 degrees on the side of the trees and anchored by further scaffold poles carefully firmed into the ground. Alternatively, the alternative specification of Heras type panels, fitted with stabiliser struts as per Figure 3 of BS5837, may be used. Clear signs will be attached at 6 metre intervals along the line of barriers stating 'Tree Protection Area – No Access'.
- 7.2 The barriers shall remain in place until soft landscape operations require their full or partial removal (see section 11). No other construction activity will take place within those areas formerly protected by the barriers (see Section 5).

8.0 Treatment of existing hard surfaces

- 8.1 Where existing hard surfaces are present within the root protection area they shall be broken up and removed using hand-held tools.
- 8.2 Roots often exist in the substrate below hard surfaces and extreme care must be taken to avoid damage to them.
- 8.3 Immediately after, the void left as a consequence of their removal shall be filled with good quality topsoil as a prelude to soft landscape unless a replacement hard surface is proposed whereupon it shall be completed in accordance with the instruction contained herein.

9.0 Creation of new hard surfacing within root protection areas

- 9.1 Areas of 'no-dig' construction shown on the drawing listed in Table 2 shall be implemented in accordance with site progress.
- 9.2 Any deleterious materials and debris deposited in the area are to be taken up by a tracked 360° excavator working from outside the root protection area. Final clearance shall be undertaken by hand picking.

- 9.3 The proposed areas of 'no-dig' construction within root protection areas shall be carried out in the following manner, subject to the manufacturers and engineers instructions.
- 9.3.1 Existing surface vegetation of grass is to be treated with approved herbicide to the manufacturer's recommendation. The surface mat may be removed to a maximum of 50mm depth.
- 9.3.2 Sharp sand is to be imported and spread over the area by hand equipment (wheelbarrows, shovels and rakes only) to bring the surface to an even level.
- 9.3.3 A geotextile material such as Fibretex F4m is to be laid on the surface of the ground in the area of the proposed car park.
- 9.3.4 A 3-dimensional cellular confinement material such as Cellweb Tree Root Protection System supplied by Geosynthetic Technologies Ltd is to be laid on top of the geotextile membrane.
- 9.3.5 Edging supports of railway sleepers or other treated timber are to be laid and pinned to the ground preferably through the cell confinement material.
- 9.3.6 The cells are to be filled with a no-fines aggregate commencing at the leading edge of the works and progressing forwards. Material can be imported to, and spread within, the working area by small excavators not exceeding 2 tonne capacity providing they work only off the filled cells area.
- 9.3.7 The final wearing course will be laid after the main construction works are complete.
- 9.3.8 Typical details of construction are shown at Appendix 1
- 9.3.9 Details of this construction must be verified by a qualified engineer.

10.0 Excavations within root protection areas

- 10.1 Excavations are proposed to install power cables within the root protection area of tree 1, an offsite poplar tree.
- 10.2 Specialist techniques shall be used for their installation to avoid material harm to the tree. Specialist techniques shall include:
- excavation using hand-held tools, air spade or vacuum.
 - trenchless installation techniques such as moling, thrust boring, directional drilling etc.

11.0 Reinstatement and landscaping

- 11.1 Final grading to marry in new levels with existing ground will be achieved by importing topsoil and spreading by hand equipment only. The newly graded areas will be grass seeded or turfed by hand.
- 11.2 All tree and shrub planting pits will be dug by hand within the root protection areas of existing trees.

12.0 Planning, communication and supervision

- 12.1 A list of useful contacts is attached at Appendix 2.
- 12.2 A pre-commencement meeting will take place on site attended by the appointed arboricultural consultant, the tree contractor and the site manager. The purpose of this meeting is to ensure that everyone fully understands the implications of the arboricultural method statement and to agree on finer points of detail prior to any works commencing.
- 12.3 The appointed arboricultural consultant shall monitor the works at the following key stages:
- 12.3.1 Commencement of installation of services / utilities with root protection areas.
- 12.4 It shall be the duty of the client to notify the arboricultural consultant when the works are ready for inspection.

- 12.5 At the completion of each monitoring visit the appointed arboricultural consultant will circulate a short monitoring report to the client, site and the local authority arboricultural officer to confirm that works are progressing satisfactorily.
- 12.6 The site manager will brief all site personnel on the implications of the arboricultural method statement. A copy of this method statement will be available on site at all times.

13.0 Transgression

- 13.1 Failure to adhere to the requirements in this method statement may result in a Stop Notice being issued by the local authority. This will bring all operations at the site to a halt until the local authority permits resumption.
- 13.2 The following measures will be required, but do not absolve the perpetrator from action, if the identified transgression occurs:
 - a) Breakage of branches – the damaged shall be assessed by an arboriculturist, they shall advise on requirements and any pruning shall be undertaken in accordance with BS3998:2010 to remove the damaged section.
 - b) Damage to bark – the damage shall be assessed by an arboriculturist and they shall advise on the measures that can be taken to optimise the reparation of the damage. Some paring back of damage may be required.
 - c) Damage to roots – the damage shall be assessed by an arboriculturist and they shall advise on the pruning or reparation required.
 - d) Compaction of soil – where machinery operates outside of ground protection and hard surfaces, leading to the compaction of soil, the compaction shall be alleviated by using compressed air injected to circa 1m deep to create fissures in the ground and lift the compacted areas. The compaction shall be assessed by an arboriculturist. A specialist company (for example Terrain Aeration Ltd) shall be appointed by the contractor to undertake the work.
- 13.4 All items of transgression shall be reported to the Local Authority tree officer to consider if action should be taken.


14.0 Conclusion

- 14.1 If the provisions of this arboricultural method statement are complied with in full, the proposed works will be able to proceed without detrimental impact to retained trees.

Appendix 1

Typical detail of no-dig construction

Figure 3: Typical detail of 'no-dig' surfacing

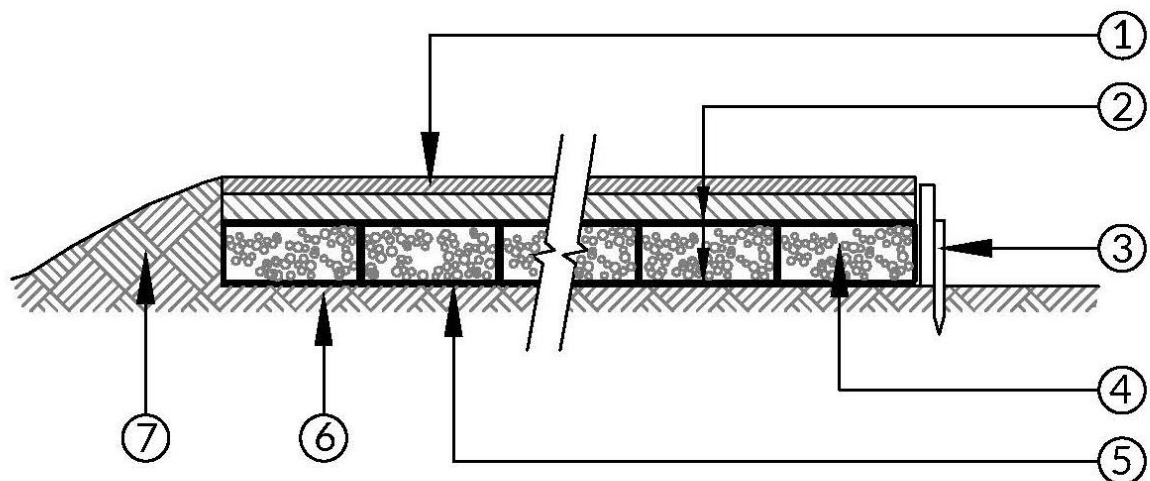

1. Surface material to engineer's specifications
2. Geotextile separation fabric as specified by engineers
3. Treated timber edging if required (sleepers can be used for a more robust edge)
4. 40/20mm clean angular stone
5. Cellular confinement system to engineer's specification and depth
6. Existing ground levels retained (no excavation)
7. Soil fillet can be used at edges

Appendix 2

List of contacts

List of contacts

Site Address:	West Sompting Phase 3, West Sussex	
Site Manager:	To be decided (TBD)	Tele No:
Builder:	TBD	
Address:		
Contact Name:	TBD	
Arboricultural Consultant:	Jago Keen	
Address:	Keen Consultants The Studio Timbers Gables Road Church Crookham Fleet Hampshire GU52 6QY	
Tele No:	01252 850096 (office)	(mobile) [REDACTED]
Local Authority	Adur District Council	
Email address:	planning@adur-worthing.gov.uk	
Telephone No.:	01903 221065	
