
Item: 6 of 6 | **Location:** Bedroom 1 | **Job Type:** Supply & Fit - Remove & replace

Surveyor Notes:

View from outside

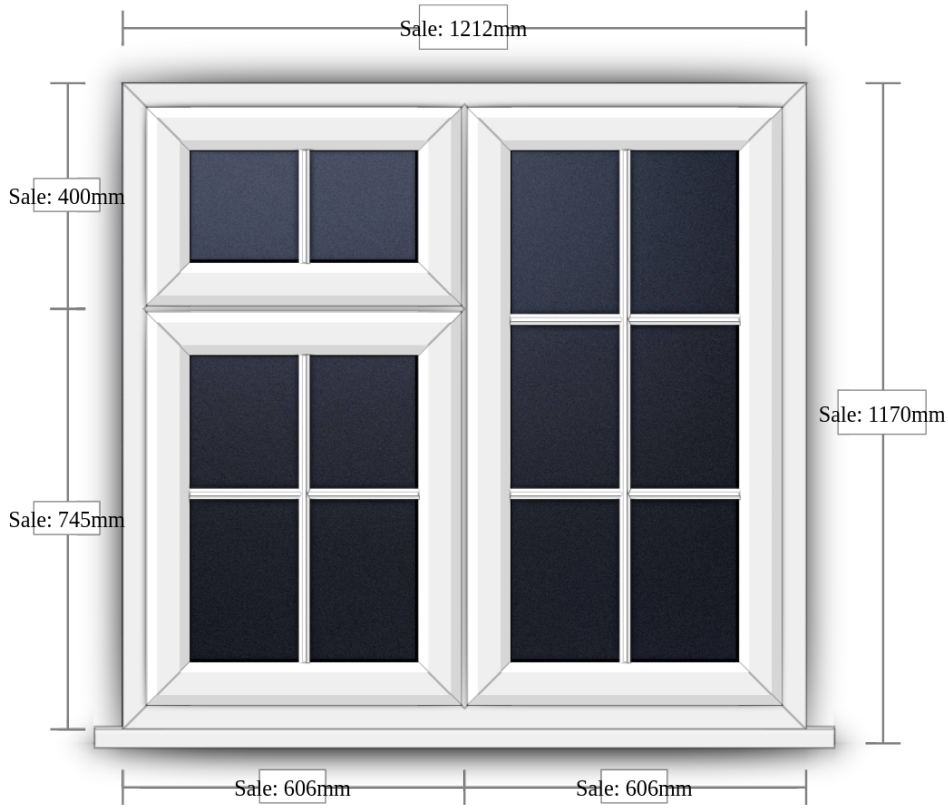

1002: Rehau Total 70 Casement

☐ **Frame**	Standard Chamfered	☐ **Cill Left Horn Length**	50mm
☐ **Sash**	Standard Chamfered	☐ **Cill Right Horn Length**	50mm
☐ **Transom**	Standard Chamfered	☐ **Addons TLRB**	None
☐ **Mullion**	Standard Chamfered	☐ **Frame Joint Type**	Welded
☐ **Sash**	Standard Bevel	☐ **Sash Joint Type**	Welded
☐ **Bead**	Sculptured	☐ **Colour**	Smooth White
☐ **Cill**	Sub Cill 150mm	☐ **Internal bar**	18MM White Georgian
☐ **Cill Length**	1312mm	☐ **Window handle**	Connoisseur White

Glass

Pane	*Description*
☐ **Pane B**	Glass: Double 4-20-4 A Rated - Black Spacer - 18MM White Georgian - Clear
☐ **Upper Pane A**	Glass: Double 4-20-4 A Rated - Black Spacer - 18MM White Georgian - Clear
☐ **Lower Pane A**	Glass: Double 4-20-4 A Rated - Black Spacer - 18MM White Georgian - Clear

Opener Hardware

Pane	*Handle*	*Drive gear*	*Hinge*	*Trickle vent*
☐ **Pane B**	Connoisseur White	No	Standard	No
☐ **Upper Pane A**	Connoisseur White	No	Standard	No

Date:	Customer:	Surveyor:
	Signature:	Signature:

Please note: Images shown are for illustrative purposes.
Printers & computer screens cannot be relied upon to accurately replicate colours.

Produced using Framepoint ® Technology
Copyright TommyTrinder.com Ltd
