
Item: 2 of 6	**Location:** Bedroom 2	**Job Type:** Supply & Fit - Remove & replace

Surveyor Notes:

View from outside

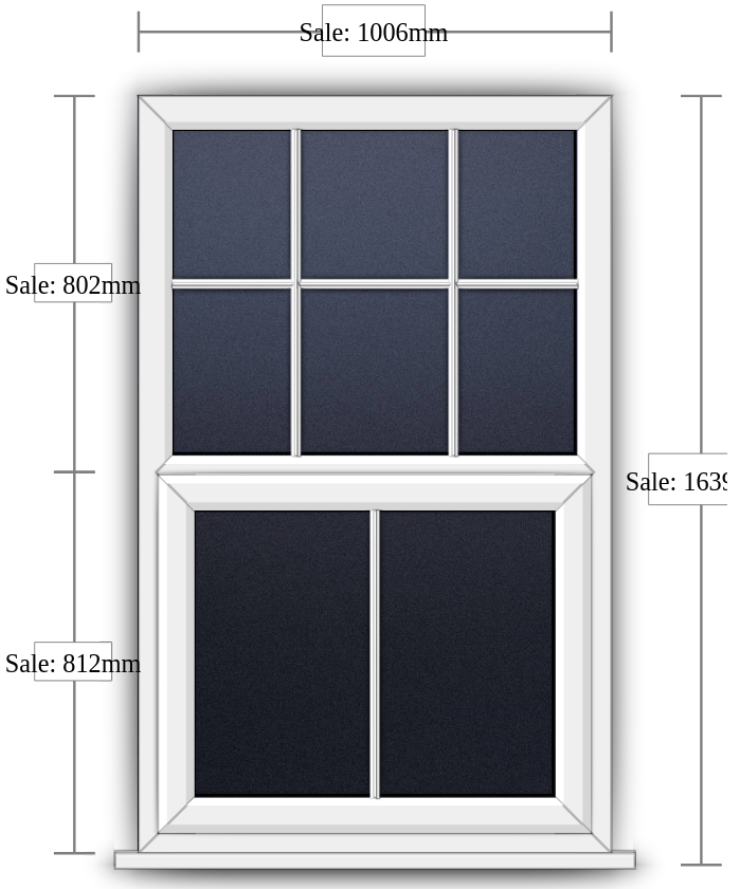

1002: Rehau Total 70 Casement

☐ **Frame**	Standard Chamfered	☐ **Cill Left Horn Length**	50mm
☐ **Sash**	Standard Chamfered	☐ **Cill Right Horn Length**	50mm
☐ **Transom**	Standard Chamfered	☐ **Addons TLRB**	None
☐ **Sash**	Standard Bevel	☐ **Frame Joint Type**	Welded
☐ **Bead**	Sculptured	☐ **Sash Joint Type**	Welded
☐ **Cill**	Sub Cill 150mm	☐ **Colour**	Smooth White
☐ **Cill Length**	1106mm	☐ **Internal bar**	18MM White Georgian

Glass

Pane	*Description*
☐ **Upper Pane**	Glass: Double Toughened 4-20-4 - Black Spacer - 18MM White Georgian - Clear
☐ **Lower Pane**	Glass: Double Toughened 4-20-4 - Black Spacer - 18MM White Georgian - Clear

Date:	Customer:	Surveyor:
	Signature:	Signature:

Please note: Images shown are for illustrative purposes.
Printers & computer screens cannot be relied upon to accurately replicate colours.

Produced using Framepoint ® Technology
Copyright TommyTrinder.com Ltd
